


ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors	Resource Initials	Sun Sep 24 2 AM	Mon Sep 25 2 PM	Tue Sep 26 2 AM	Wed Sep 27 2 PM	Thu Sep 28 2 AM	Fri Sep 29 2 AM	Sat Sep 30 2 AM	Sun Oct 01 2 PM	Mon Oct 02 2 AM	Tue Oct 03 2 PM	Wed Oct 04 2 PM
0		ASP.NET Core Project	5 days	Mon 23-09-25	Sun 23-10-01													
1		Inception	5 days	Mon 23-09-25	Sun 23-10-01													
2		Inception I1	6 days	Mon 23-09-25	Sun 23-10-01													
3	✓	Project Kickoff	1 day	Mon 23-09-25	Mon 23-09-25		AMLR,SD											
4	✓	Initial User Interview	1.13 days	Tue 23-09-26	Wed 23-09-27													
5	✓	Develop Interview Questions	1 day	Tue 23-09-26	Tue 23-09-26	3	AMLR,SD											
6	✓	First Interview With Stakeholders	1 hr	Wed 23-09-27	Wed 23-09-27	5	AMLR,SD											
7		Project Documentation	4 days	Tue 23-09-26	Fri 23-09-29													
8	✓	Create Iteration Plan for Inception I1	1 day	Tue 23-09-26	Tue 23-09-26	3	AMLR,SD											
9	✓	Create Contract of Participaton	1 day	Tue 23-09-26	Tue 23-09-26	3	AMLR,SD											
10	✓	Create Client Profile Document	1 day	Tue 23-09-26	Tue 23-09-26	3	SD											
11		Weekly Status Update Video	1 day	Fri 23-09-29	Fri 23-09-29	13	AMLR,SD											
12		Create Iteration Plan for Elaboration E1	1 day	Fri 23-09-29	Fri 23-09-29	13	AMLR,SD											
13	👤	Wireframe Diagrams	3 days	Tue 23-09-26	Thu 23-09-28	3	AMLR,SD											
14	👤	Login Wireframes	1 day	Tue 23-09-26	Tue 23-09-26		SD											
15	👤	Navigation Layout Wireframes	1 day	Wed 23-09-27	Wed 23-09-27	14	SD											
16	👤	Customer Creation Wireframes	1 day	Tue 23-09-26	Tue 23-09-26		AMLR											
17	👤	Agent Creation Wireframes	1 day	Tue 23-09-26	Tue 23-09-26		AMLR											
18	👤	Image Upload Portal Wireframes	1 day	Thu 23-09-28	Thu 23-09-28	15	SD											
19		User Walkthrough for Inception I1	1 hr	Fri 23-09-29	Fri 23-09-29	13	AMLR,SD											
20		End of Inception Phase	0 days	Sun 23-10-01	Sun 23-10-01		AMLR,SD											

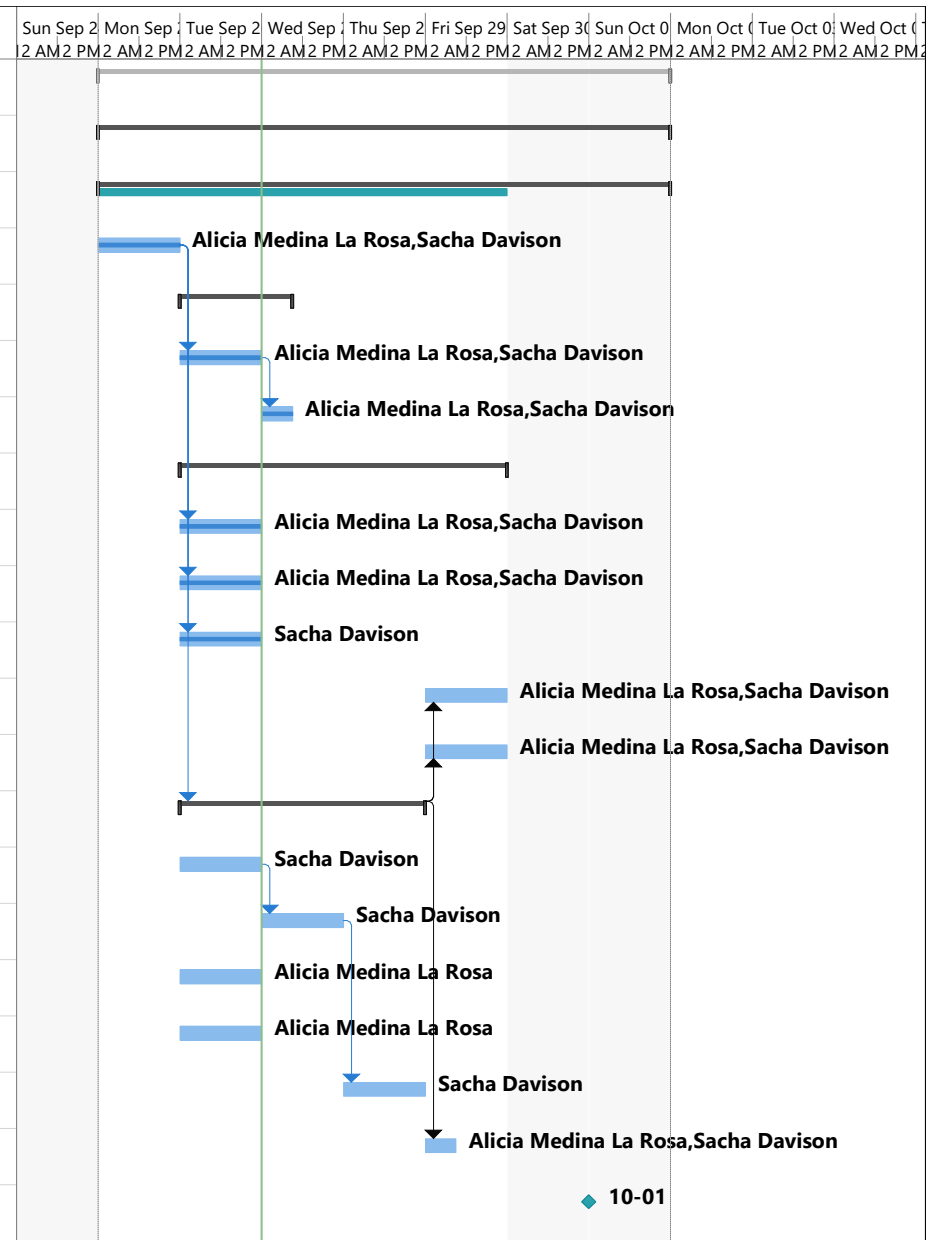


Project: ASP.NET Core Project Date: Wed 23-09-27	Task		Project Summary		Manual Task		Start-only		Deadline	
	Split		Inactive Task		Duration-only		Finish-only		Progress	
	Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
	Summary		Inactive Summary		Manual Summary		External Milestone			

ID	Task Name	Duration	Start	Finish	Predecessors	'23 Oct 22							'23 Oct 29							'23 Nov 05	
						M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	
0	ASP.NET Core Project	21.75 days	Mon 23-10-16	Mon 23-11-06																	
1	Elaboration	21 days?	Mon 23-10-16	Sun 23-11-05																	
2	Iteration E2	21 days?	Mon 23-10-16	Sun 23-11-05																	
3	Implement Use Case: Save Listing	4 days	Tue 23-10-17	Fri 23-10-20																	
4	Implement Data Model for Listing	1 day	Tue 23-10-17	Tue 23-10-17																	
5	Implement Logic for Save Listing	1 day	Tue 23-10-17	Wed 23-10-18	4																
6	Generate View(s) for Save Listing	2 days	Wed 23-10-18	Fri 23-10-20	5																
7	Implement Use Case: Upload Image	4 days	Tue 23-10-17	Fri 23-10-20																	
8	Update Data Model for Image	1 day	Tue 23-10-17	Tue 23-10-17																	
9	Update Logic for Upload Image	1 day	Tue 23-10-17	Wed 23-10-18	8																
10	Update View(s) for Upload Image	2 days	Wed 23-10-18	Fri 23-10-20	9																
11	Implement Use Case: Save Showing	3 days	Fri 23-10-20	Mon 23-10-23	3																
12	Implement Data Model for Save Showing	1 day	Fri 23-10-20	Sat 23-10-21	3																
13	Implement Logic for Save Showing	1 day	Sat 23-10-21	Sun 23-10-22	12,3																
14	Generate View(s) for Save Showing	1 day	Mon 23-10-23	Mon 23-10-23	13,3																
15	Stakeholder Communications	15 days	Fri 23-10-20	Fri 23-11-03																	
16	E2 Week 1 Status Update	1 hr	Fri 23-10-20	Fri 23-10-20																	
17	E2 Week 2 Status Update	1 hr	Fri 23-10-27	Fri 23-10-27	16																
18	E2 Week 3 Status Update	1 hr	Fri 23-11-03	Fri 23-11-03	17																
19	Integration Activities	1 day	Sat 23-10-21	Sat 23-10-21	3,11,7,15																
20	Unit Testing	1 day	Sat 23-10-21	Sat 23-10-21	3,11,7,15																
21	Save Showing Unit Test	2 hrs	Sat 23-10-21	Sat 23-10-21	3,11,7,15																
22	Save Listing Unit Test	2 hrs	Mon 23-10-23	Mon 23-10-23	3,11,7,15																
23	Upload Image Unit Test	2 hrs	Sat 23-10-21	Sat 23-10-21	3,11,7,15																
24	Integration Testing	1 day	Tue 23-10-24	Tue 23-10-24	20																
25	User Walkthrough (E1)	3 days	Tue 23-10-31	Thu 23-11-02	3,11,7,15																
26	Schedule Walkthrough With Client	1 hr	Tue 23-10-31	Tue 23-10-31	3,11,7,15																
27	User Walkthrough Interview	1 hr	Thu 23-11-02	Thu 23-11-02	26																
28	Product Release Milestone - v0.1	0 days	Sun 23-11-05	Sun 23-11-05	26																
29	Create E2 Iteraion Plan	2 days	Sun 23-11-05	Mon 23-11-06	3,11,7,15																
30	End of Iteration E1	0 days	Sun 23-11-05	Sun 23-11-05																	

Project: ASP.NET Core Project Date: Mon 23-10-16	Task		Project Summary		Manual Task		Start-only		Deadline	
	Split		Inactive Task		Duration-only		Finish-only		Progress	
	Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
	Summary		Inactive Summary		Manual Summary		External Milestone			


ID	Task Name	Duration	Start	Finish	Predecessors	Resource Initials	'23 Nov 05	'23 Nov 12	'23 Nov 19													
							S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M
0	ASP.NET Core Project	13.88 days	Mon 23-11-06	Sun 23-11-19																		
1	Construction	14 days	Mon 23-11-06	Sun 23-11-19		SD,AMLR																
2	Iteration C1	14 days	Mon 23-11-06	Sun 23-11-19		AMLR,SD																
3	Implement Use Case: Assign User Authorization	3 days	Mon 23-11-06	Wed 23-11-08		SD																
4	Implement Data Model for Assign User Authorization	1 day	Mon 23-11-06	Mon 23-11-06		SD																
5	Implement Logic for Assign User Authorization	1 day	Mon 23-11-06	Tue 23-11-07	4	SD																
6	Generate View(s) for Assign User Authorization	1 day	Tue 23-11-07	Wed 23-11-08	5	SD																
7	Implement Use Case: View Listing	3 days	Mon 23-11-06	Wed 23-11-08		AMLR																
8	Implement Data Model for View Listing	1 day	Mon 23-11-06	Mon 23-11-06		AMLR																
9	Implement Logic for View Listing	1 day	Mon 23-11-06	Tue 23-11-07	8	AMLR																
10	Generate View(s) for View Listing	1 day	Tue 23-11-07	Wed 23-11-08	9	AMLR																
11	Implement Use Case: Renew Listing Contract	3 days	Wed 23-11-08	Fri 23-11-10	7	AMLR																
12	Implement Data Model for Renew Listing Contract	1 day	Wed 23-11-08	Wed 23-11-08		AMLR																
13	Implement Logic for Renew Listing Contract	1 day	Wed 23-11-08	Thu 23-11-09	12	AMLR																
14	Generate View(s) for Renew Listing Contract	1 day	Thu 23-11-09	Fri 23-11-10	13	AMLR																
15	Implement Use Case: Generate Listing Report	3 days	Wed 23-11-08	Fri 23-11-10		SD																
16	Implement Data Model for Generate Listing Report	1 day	Wed 23-11-08	Wed 23-11-08		SD																
17	Implement Logic for Generate Listing Report	1 day	Thu 23-11-09	Thu 23-11-09	16	SD																
18	Generate View(s) for Generate Listing Report	1 day	Fri 23-11-10	Fri 23-11-10	17	SD																
19	C1 Weekly Status Update	7 days	Fri 23-11-10	Thu 23-11-16		SD,AMLR																
20	C1 Weekly Status Update 1	1 day	Fri 23-11-10	Fri 23-11-10		SD,AMLR																
21	C1 Weekly Status Update 2	1 day	Fri 23-11-17	Fri 23-11-17		SD,AMLR																
22	Integration Activities	5 days	Wed 23-11-08	Mon 23-11-13		AMLR,SD																
23	Unit Testing	4 days	Wed 23-11-08	Sun 23-11-12	7,11,15,3	AMLR,SD																
24	View Listing Unit Test	1 day	Wed 23-11-08	Thu 23-11-09	7	SD,AMLR																
25	Renew Listing Contract Unit Test	1 day	Fri 23-11-10	Sat 23-11-11	11	SD,AMLR																
26	Generate Listing Report Unit Test	1 day	Wed 23-11-08	Thu 23-11-09	15	SD,AMLR																
27	Assign User Authorization Unit Test	1 day	Fri 23-11-10	Sat 23-11-11	3	AMLR,SD																
28	Integration Testing	2 days	Sat 23-11-11	Mon 23-11-13	23	AMLR,SD																
29	User Walkthrough (C1)	1 day	Wed 23-11-15	Wed 23-11-15	22	AMLR,SD																
30	Schedule Walkthrough With Client	0.5 hrs	Wed 23-11-15	Wed 23-11-15		SD																
31	User Walkthrough Interview	0.5 hrs	Thu 23-11-16	Thu 23-11-16		AMLR,SD																
32	Product Release Milestone - v0.3	0 days	Fri 23-11-17	Fri 23-11-17		SD,AMLR																
33	Create T1 Iteraion Plan	1 day	Sat 23-11-18	Sat 23-11-18		AMLR,SD																
34	End of Iteration C1	0 days	Sun 23-11-19	Sun 23-11-19		SD,AMLR																

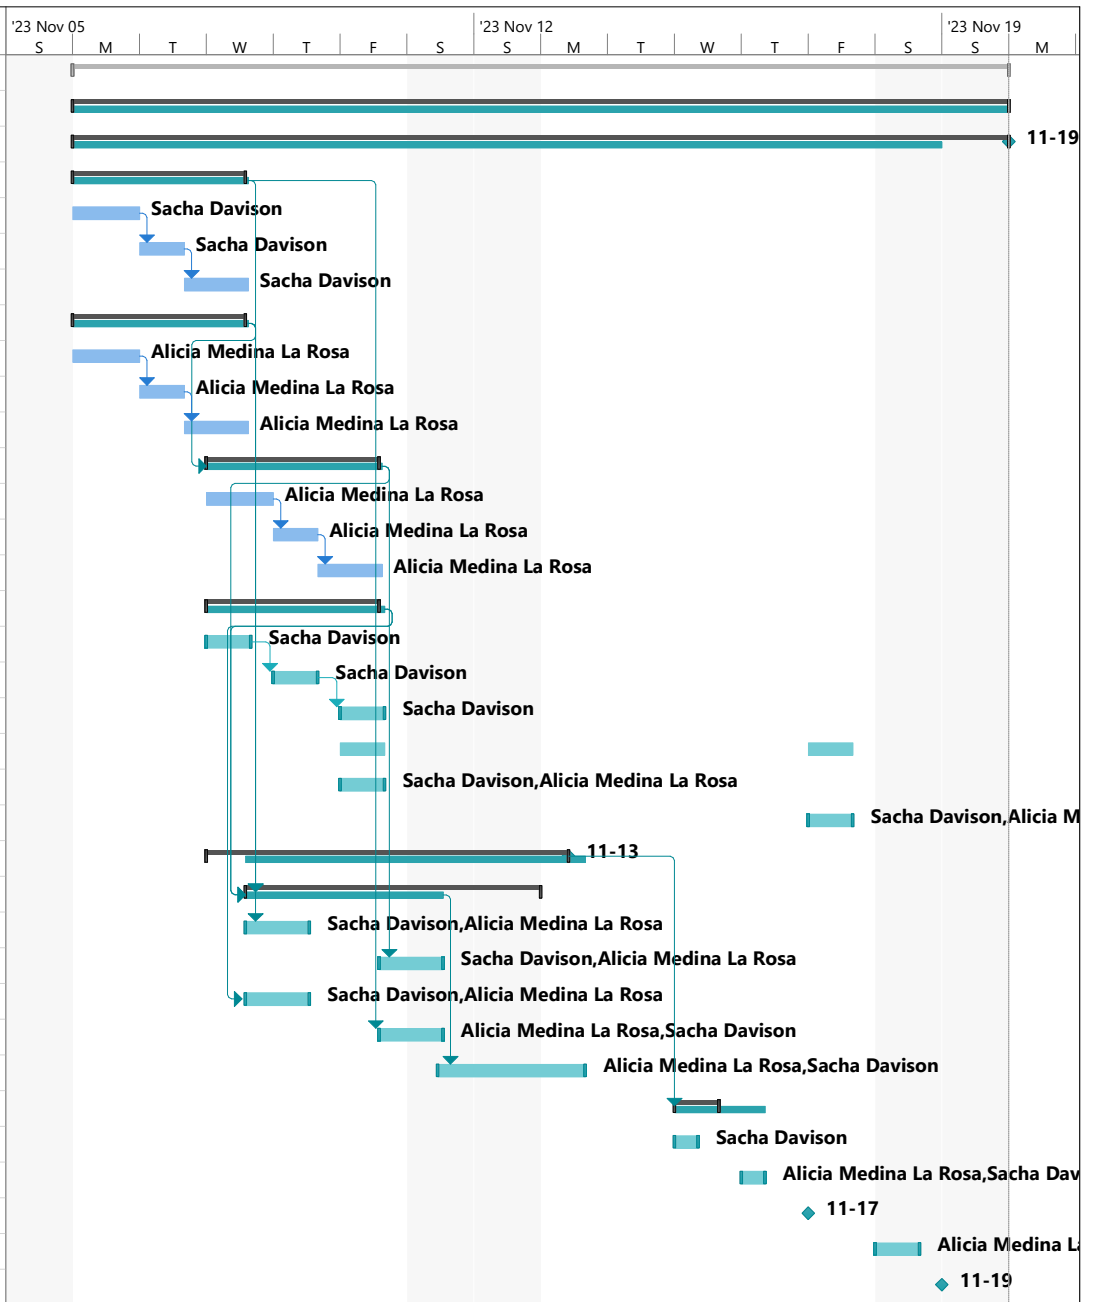

Project: ASP.NET Core Project
Date: Sun 23-11-05

Task		Project Summary		Manual Task		Start-only		Manual Summary Rollup		External Tasks		Manual Progress		External Milestone		Deadline			Progress			Manual Progress	
Split		Inactive Task		Duration-only		Finish-only		Manual Summary		External Milestone		Manual Progress		External Milestone		Deadline			Progress			Manual Progress	
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Summary		External Milestone		Manual Progress		External Milestone		Deadline			Progress			Manual Progress	
Summary		Inactive Summary		Manual Summary		External Milestone		Manual Summary		External Milestone		Manual Progress		External Milestone		Deadline			Progress			Manual Progress	

ID	Task Name	Duration	Start	Finish	Predecessors	Resource Initials	Nov 19 12 PM	Mon Nov 20 12 AM 12 PM	Tue Nov 21 12 AM 12 PM	Wed Nov 22 12 AM 12 PM	Thu Nov 23 12 AM 12 PM	Fri Nov 24 12 AM 12 PM	Sat Nov 25 12 AM 12 PM	Sun Nov 26 12 AM 12 PM	Mon Nov 27 12 AM 12 PM
0	ASP.NET Core Project	7 days?	Mon 23-11-20	Sun 23-11-26											
1	Transition	7 days?	Mon 23-11-20	Sun 23-11-26		SD,AMLR									
2	Iteration T1	7 days?	Mon 23-11-20	Sun 23-11-26		AMLR,SD									11-26
3	Corrections	2 days	Mon 23-11-20	Tue 23-11-21		SD,AMLR									
4	Implement Corrections for Previous Iterations	2 days	Mon 23-11-20	Tue 23-11-21		SD,AMLR									
5	Integration Activities	3 days	Tue 23-11-21	Fri 23-11-24	3,4	SD,AMLR									
6	Unit Testing	2 days	Tue 23-11-21	Thu 23-11-23		SD,AMLR									
7	Create Agent Unit Tests	0.5 days	Tue 23-11-21	Wed 23-11-22		SD,AMLR									
8	Create Customer Unit Tests	0.5 days	Tue 23-11-21	Wed 23-11-22		AMLR,SD									
9	Upload Image Unit Tests	0.5 days	Tue 23-11-21	Wed 23-11-22		SD,AMLR									
10	Save Listing Unit Tests	0.5 days	Wed 23-11-22	Wed 23-11-22	7,8,9	SD,AMLR									
11	Save Showing Unit Tests	0.5 days	Wed 23-11-22	Thu 23-11-23	7,8,9,10	SD,AMLR									
12	View Listing Unit Tests	0.5 days	Thu 23-11-23	Thu 23-11-23	7,8,9,10,11	SD,AMLR									
13	Renew Listing Contract Unit Tests	0.5 days	Thu 23-11-23	Thu 23-11-23	7,8,9,10,11	SD,AMLR									
14	Generate Listing Report Unit Tests	0.5 days	Thu 23-11-23	Thu 23-11-23	7,8,9,10,11	AMLR,SD									
15	Assign Admin Authorization Unit Tests	0.5 days	Thu 23-11-23	Thu 23-11-23	7,8,9,10,11	AMLR,SD									
16	Integration Testing	1 day	Thu 23-11-23	Fri 23-11-24	6	SD,AMLR									
17	System Testing	1 day	Thu 23-11-23	Fri 23-11-24	6	SD,AMLR									
18	Bug Fixes	1 day	Thu 23-11-23	Fri 23-11-24	6	SD,AMLR									
19	Weekly Status Updates	0 days	Fri 23-11-24	Fri 23-11-24		SD									
20	Weekly Status Update	0 days	Fri 23-11-24	Fri 23-11-24		SD									
21	Presentation Preparation	2 days	Fri 23-11-24	Sun 23-11-26		SD,AMLR									
22	Test Data	1 day	Fri 23-11-24	Sat 23-11-25		SD,AMLR									
23	Generate Presentation Test Data	0.5 days	Fri 23-11-24	Fri 23-11-24	5	SD									
24	Verify Test Data Meets Requirements	0.5 days	Fri 23-11-24	Sat 23-11-25	5,23	AMLR									
25	Presentation Rehearsals	1 day	Sat 23-11-25	Sun 23-11-26	22	SD,AMLR									
26	Presentation Rehearsal 1	0.5 days	Sat 23-11-25	Sat 23-11-25	22	SD,AMLR									
27	Presentation Rehearsal 2	0.5 days	Sat 23-11-25	Sun 23-11-26	26	SD,AMLR									
28	Product Release Milestone - v1.0	0 days	Fri 23-11-24	Fri 23-11-24		SD,AMLR									
29	End of Iteration T1	0 days	Sun 23-11-26	Sun 23-11-26		SD,AMLR									

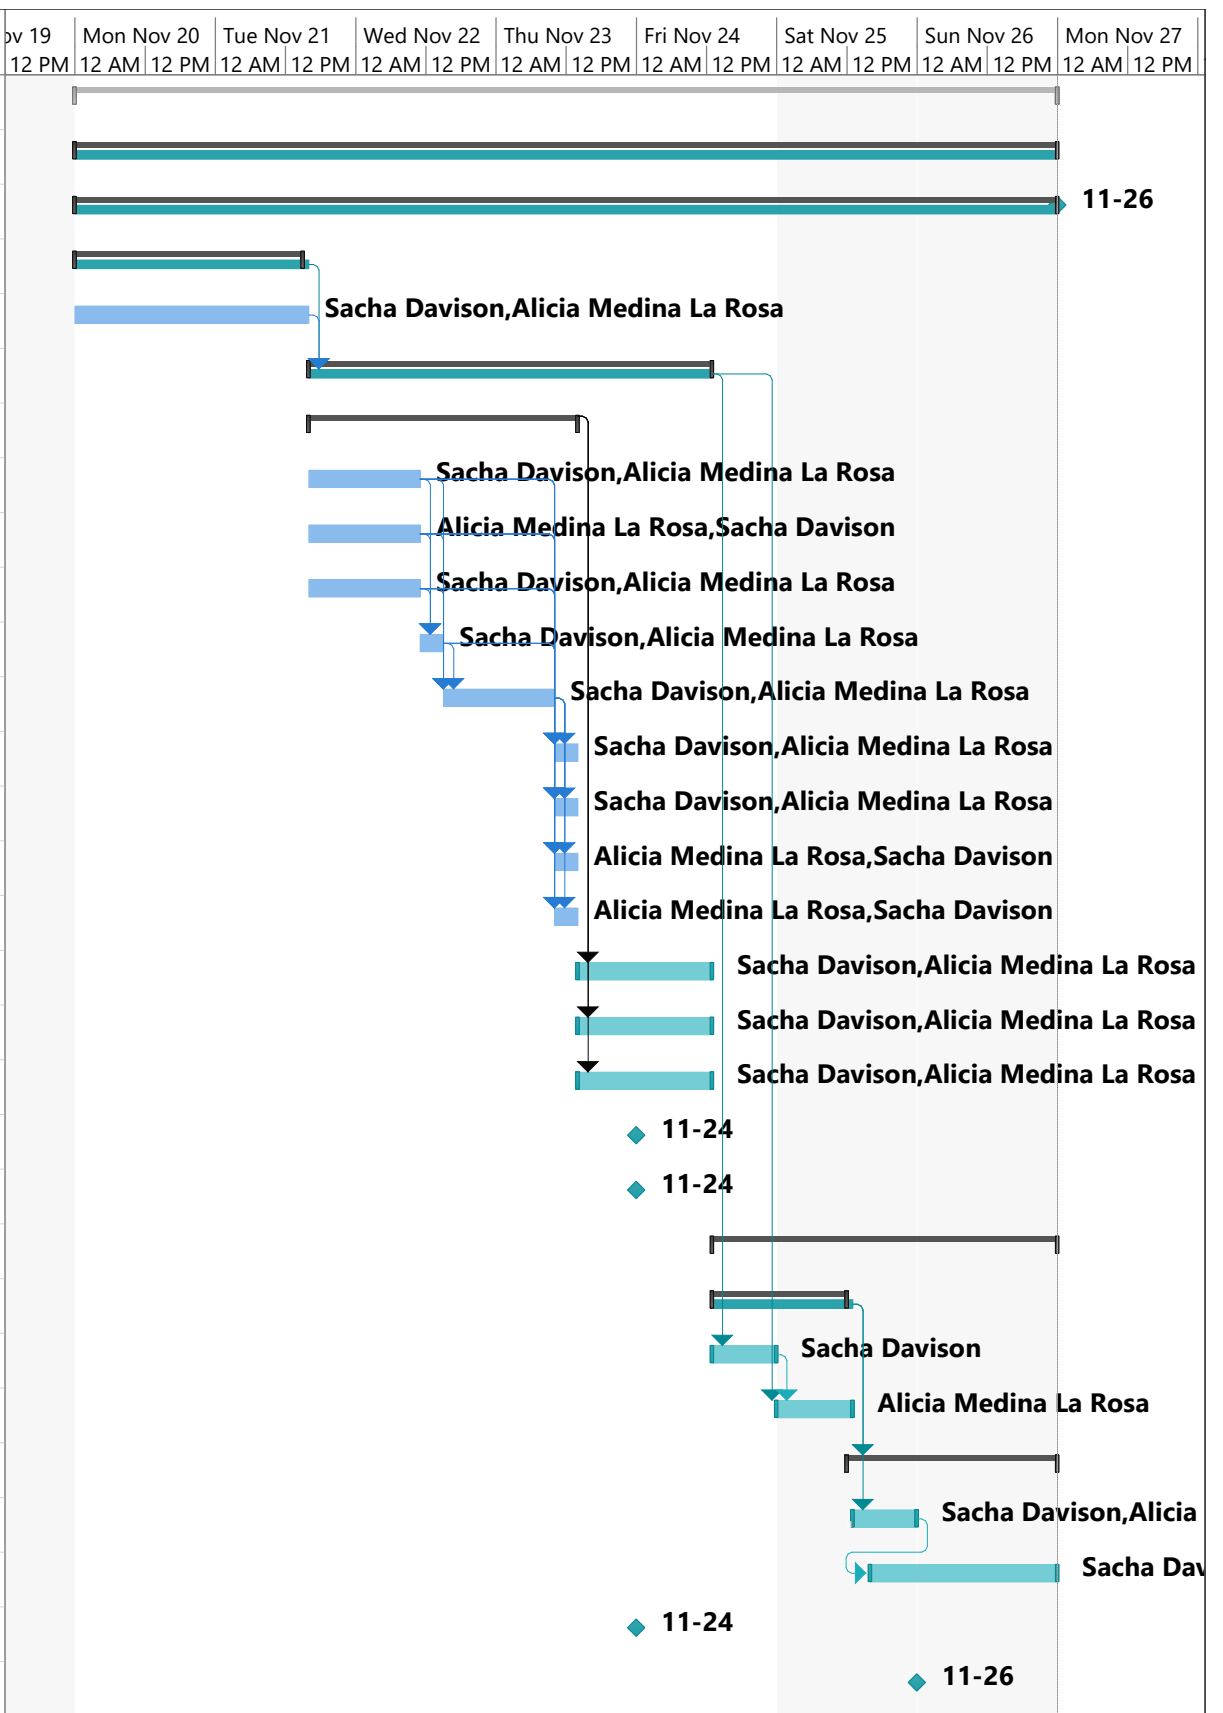

Project: ASP.NET Core Project Date: Sat 23-11-18	Task		Project Summary		Manual Task		Start-only		Deadline	
	Split		Inactive Task		Duration-only		Finish-only		Progress	
	Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
	Summary		Inactive Summary		Manual Summary		External Milestone			
